

SR26, ATLANTIC AVE. FROM CLARKSVILLE TO ASSAWOMAN CANAL
DELDOT CONTRACT NO. T200411210
SR26 WORKING GROUP

SR26 WORKING GROUP

Meeting No. 2

January 28, 2013




SR26, ATLANTIC AVE. FROM CLARKSVILLE TO ASSAWOMAN CANAL
DELDOT CONTRACT NO. T200411210
SR26 WORKING GROUP

Opening Remarks



SR26, ATLANTIC AVE. FROM CLARKSVILLE TO ASSAWOMAN CANAL
 DELDOT CONTRACT NO. T200411210
SR26 WORKING GROUP

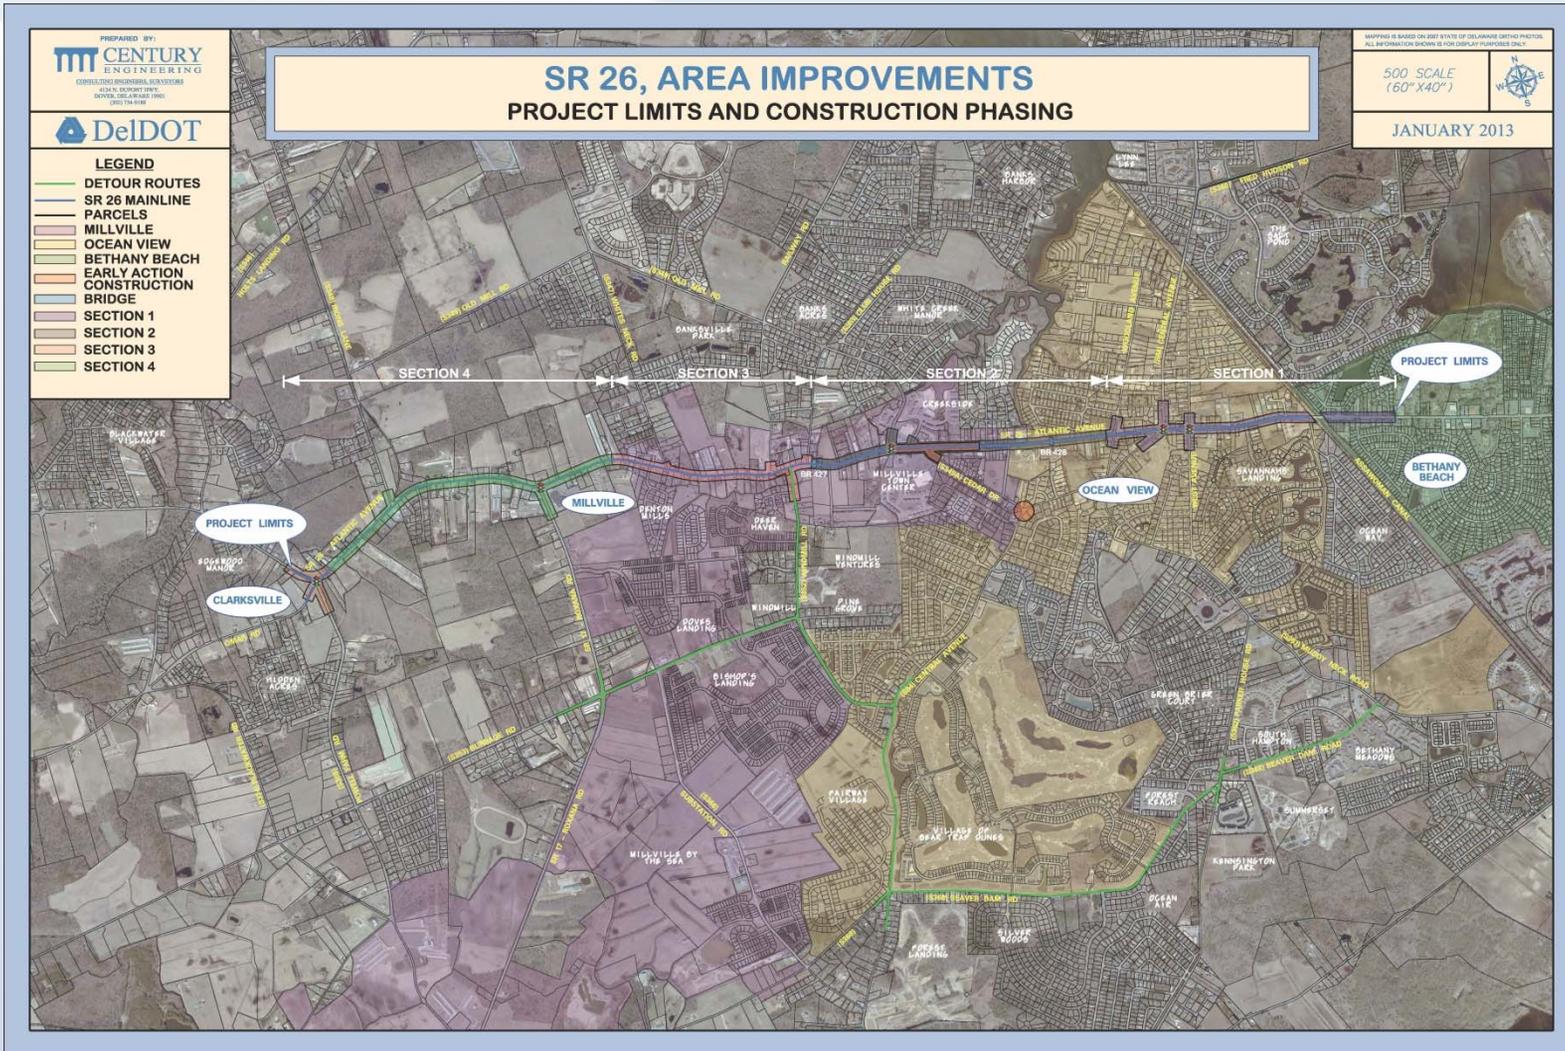

➤ **Agenda**

- **Introduction**
 - Project Commitment
- **Project Status Update (SR 26 Detour Routes)**
 - Construction Update
- **Project Status Update (SR 26 Mainline)**
 - Utility Relocations
 - Real Estate Acquisitions
 - Advertisement Schedule
 - Construction Schedule

➤ **Agenda**

- **Review of Night Work Survey**
- **Utility Company Updates**
- **Advanced Clearing**
- **Proposed Lane Closure Restrictions**
- **Managing Traffic During Construction**
 - Advanced Message Boards
 - Alternate Routes
 - ITMS Strategies

➤ **Agenda**

- **Project Public Outreach**
 - Before Construction
 - During Construction
- **Continued Working Group Coordination**
 - Monthly to Quarterly Meetings
 - Timely Updates – SR 26 Blog
 - Website – www.SR26.deldot.gov

➤ **Project Status**

- **SR 26 Detour Routes (Work Completed)**



- SR 17
- Burbage Road
- Windmill Road at SR 26
- Beaver Dam Road between Parker House and Muddy Neck Roads


➤ Project Status

- **SR26 Detour Routes**



- Lane closures for some work
- Road closures to continue
- Coordination with subdivision entrances
- Working to expedite completion date
- No overlaps with SR26 Construction

SR26, ATLANTIC AVE. FROM CLARKSVILLE TO ASSAWOMAN CANAL
 DELDOT CONTRACT NO. T200411210
SR26 WORKING GROUP

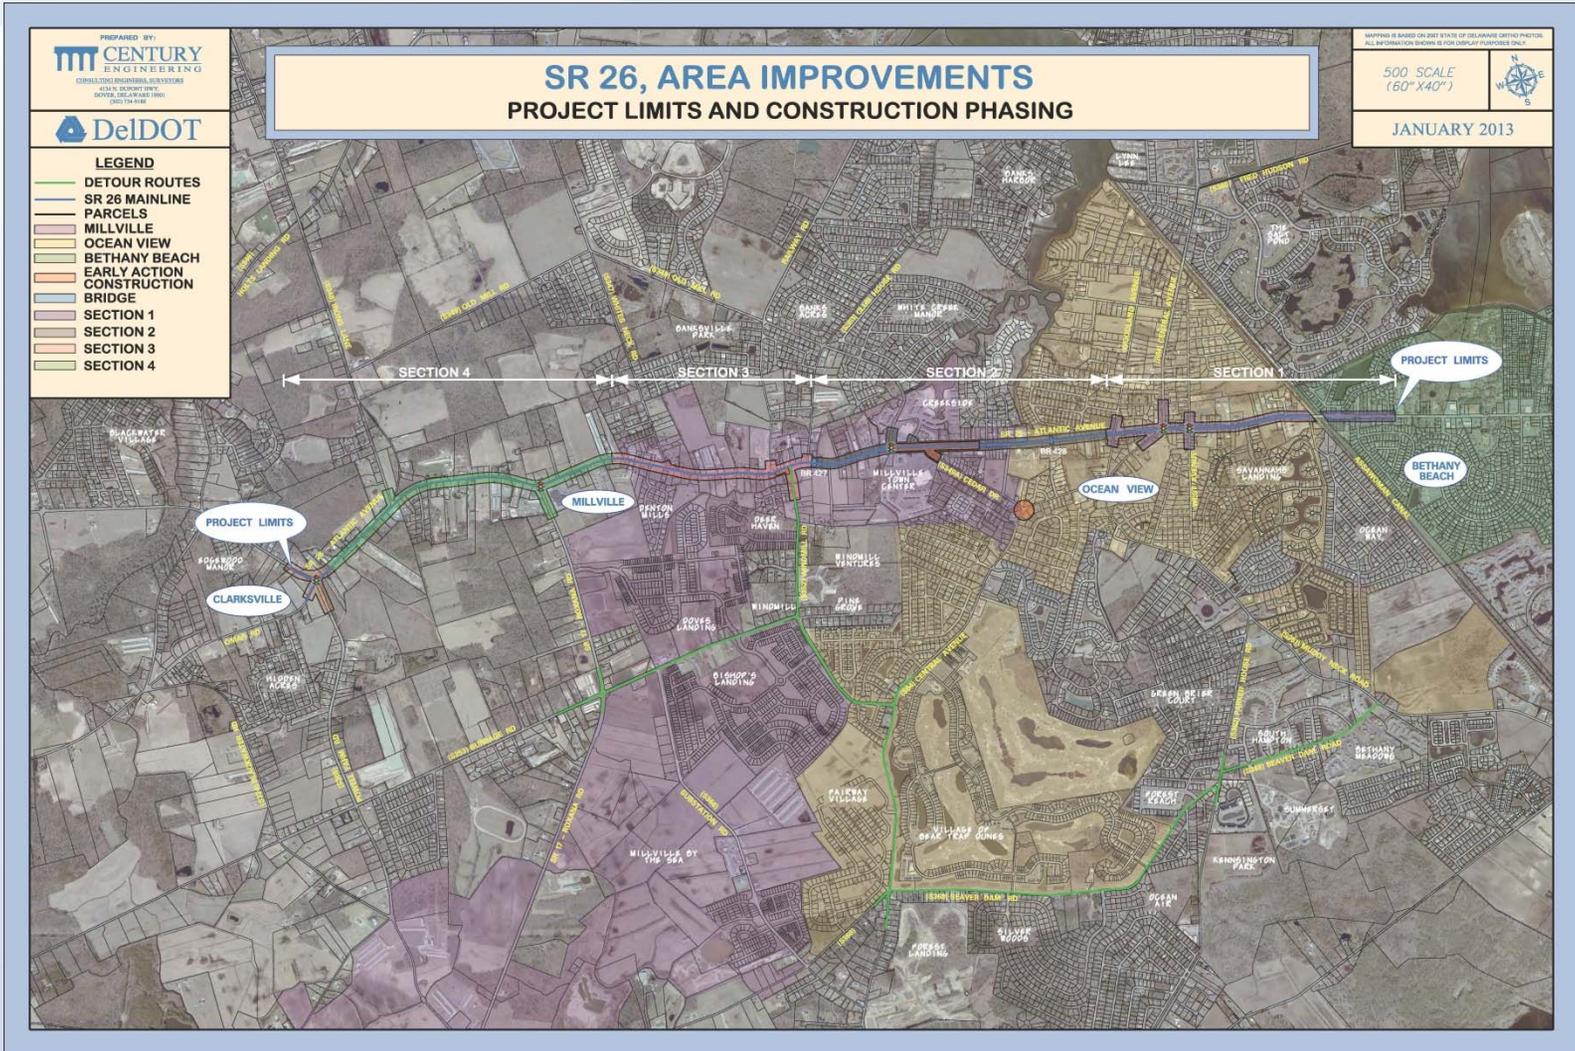

➤ Project Status

- **Utility Relocations**



- Early Action Work Completed
- Continuing Utility Pole Relocations
- Daily Communication between field and office
- Weekly Field Coordination Meetings
- Monthly Office Coordination Meetings

➤ **Project Status**

- **Real Estate Acquisitions**
 - 10 parcels outstanding (5 owners)
 - 200+ parcels acquired
- **Advertisement**
 - Anticipate Advertisement in Summer 2013
- **Construction**
 - Anticipate Construction in Fall 2013

➤ **Night Work Survey Results**

- **194** Surveys sent out to businesses and residents
- **68** responded **YES**
- **9** responded **NO**
- **117** did not respond

- **Night Work will be utilized on this project**

➤ **Upcoming Work**

- **Utility Coordination Update**
 - Verizon
 - Delmarva
 - Mediacom
- **Advanced Clearing Contract**
 - Bids Expected February 1, 2013
 - Clearing between Assawoman Canal and Railway Road

➤ Lane Closure Restrictions

- Different Peak/Off Peak Restrictions
- Holiday Restrictions during both seasons
- Maintain access to all residents and businesses during construction
- Limit the complete road closure to Winter months (January 3 – March 31)

➤ Lane Closure Restrictions

- Limit the Length of Lane Closures
- Limit the Number of Lane Closures
- Bicycle and Pedestrian Traffic will be maintained through the work zones
- Maintaining the Evacuation Route

➤ Lane Closure Restrictions

OFF-PEAK (OCTOBER 1 - MAY 15)																							
MONDAY - FRIDAY																							
12:00 AM	1:00 AM	2:00 AM	3:00 AM	4:00 AM	5:00 AM	6:00 AM	7:00 AM	8:00 AM	9:00 AM	10:00 AM	11:00 AM	12:00 PM	1:00 PM	2:00 PM	3:00 PM	4:00 PM	5:00 PM	6:00 PM	7:00 PM	8:00 PM	9:00 PM	10:00 PM	11:00 PM
Green						Red						Green											
Lane Restrictions NOT allowed between 6 am - 9 am Mondays - Fridays																							
SATURDAY																							
Green																							
No Restrictions for work on Saturdays																							
SUNDAY																							
Green																							
No Restrictions for work on Sundays																							
ON-PEAK (MAY 16 - SEPTEMBER 30)																							
MONDAY																							
Red						Green																	
Lane Restrictions only allowed between 7 pm Monday evening and 6 am Friday morning																							
TUESDAY - THURSDAY																							
Yellow						Green																	
Lane Restrictions only allowed between 7 pm Monday evening and 6 am Friday morning																							
FRIDAY																							
Green						Red																	
No Lane Restrictions allowed between 6 am Friday Morning and 7 pm Monday evening																							
SATURDAY AND SUNDAY																							
Red																							
No Lane Restrictions allowed between 6 am Friday Morning and 7 pm Monday evening																							

Green – Lane Restrictions Allowed

Red – No Lane Restrictions Allowed

➤ Lane Closure Restrictions

- **Peak Season Restrictions (May 16 – Sept. 30)**
 - Lane Closures permitted between 7 pm and 6 am Monday Night through Friday Morning
 - Lane Closures, Shoulder Closures and Lane shifts NOT permitted between 6 am Friday until 7 pm Monday

➤ Lane Closure Restrictions

- **Off-Peak Season Restrictions (Oct. 1 – May 15)**
 - Lane Closures are NOT Permitted between 6 am and 9 am Sunday through Saturday
 - Complete Road Closure with Detours will be used during Bridge Construction

➤ **Lane Closure Restrictions**

- **Learning from Previous Projects**
 - Additional notes and details added
 - Material deliveries
 - Type of Equipment being used
 - Lane Closure Restrictions
 - Public Information Meetings before and during construction
 - Working Group Meetings during construction


➤ **Managing Traffic During Construction**

- **Use of Advance Message Boards**
 - Boards will be placed outside of project limits to inform the public of the overall project
 - Boards will be placed within the project limits to give the public project specific information

➤ **Managing Traffic During Construction**

- **Signing of Alternate Routes During Construction**
 - Shifting through traffic off of SR 26
- **Detour Route for Bridge Closures**
- **Business Open Signs**
 - While through traffic will be encouraged to use the Alternate Routes, the public will be informed that all businesses within the project limits are open


SR26, ATLANTIC AVE. FROM CLARKSVILLE TO ASSAWOMAN CANAL
 DELDOT CONTRACT NO. T200411210
SR26 WORKING GROUP

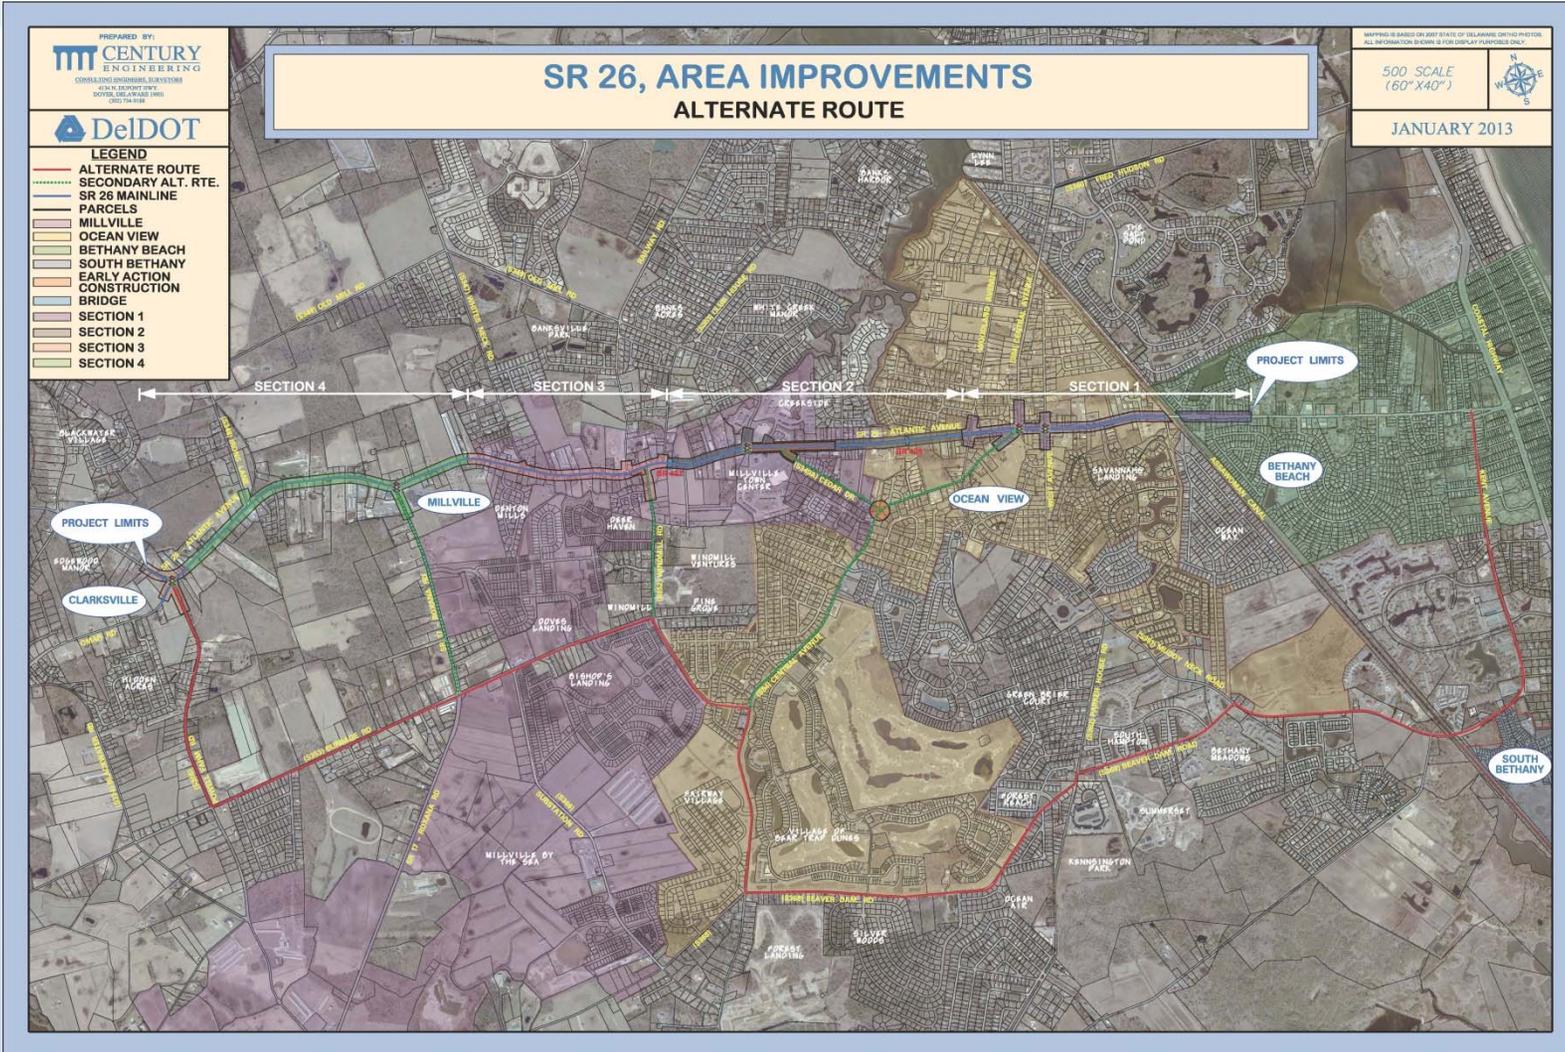

➤ **Managing Traffic During Construction**

- **Signing of Alternate Routes During Construction**
 - Shifting through traffic off of SR 26
- **Detour Route for Bridge Closures**
- **Business Open Signs**
 - While through traffic will be encouraged to use the Alternate Routes, the public will be informed that all businesses within the project limits are open

SR26, ATLANTIC AVE. FROM CLARKSVILLE TO ASSAWOMAN CANAL
 DELDOT CONTRACT NO. T200411210
SR26 WORKING GROUP

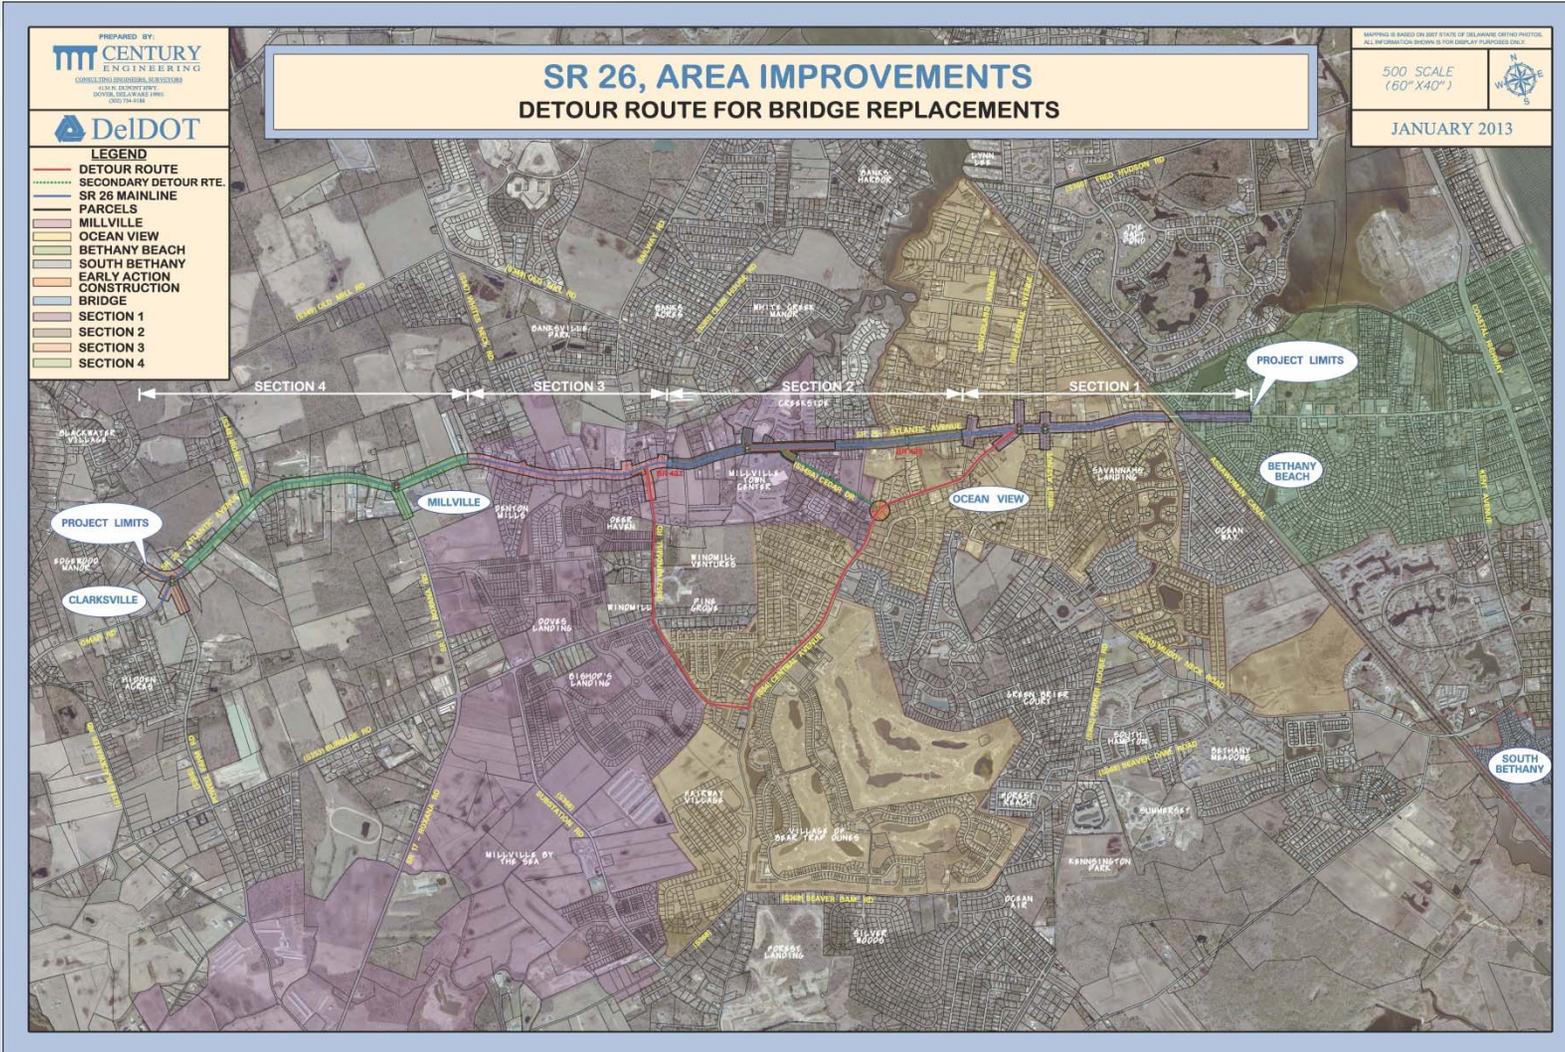

➤ **Managing Traffic During Construction**

- **Signing of Alternate Routes During Construction**
 - Shifting through traffic off of SR 26
- **Detour Route for Bridge Closures**
- **Business Open Signs**
 - While through traffic will be encouraged to use the Alternate Routes, the public will be informed that all businesses within the project limits are open

➤ **Managing Traffic During Construction**

- **ITMS Strategies**
 - Traffic Camera at SR 26 and Central Avenue
 - All signals within the project limits are “on-system”
 - Traffic can be monitored at the TMC
 - Signals (timing) can be adjusted at the TMC
 - Changeable Message Signs on US 113 North of Milford
 - Radio Announcements
 - DeIDOT Smartphone App

SR26, ATLANTIC AVE. FROM CLARKSVILLE TO ASSAWOMAN CANAL
DELDOT CONTRACT NO. T200411210
SR26 WORKING GROUP



➤ **Managing Traffic During Construction**

- **ITMS Strategies**
 - Traffic Camera at SR 26 and Central Avenue
 - All signals within the project limits are “on-system”
 - Traffic can be monitored at the TMC
 - Signals (timing) can be adjusted at the TMC
 - Changeable Message Signs on US 113 North of Milford
 - Radio Announcements
 - DeIDOT Smartphone App

➤ **Project Public Outreach**

- **Before Construction**
 - Public Information Meeting to be held before Advertisement
 - Public Information Meeting to be held during construction
- **On-Going Coordination**
 - Existing features within Right of Way
 - Property owner questions
 - Request for information

➤ **Project Public Outreach**

- **During Construction**
 - Press Releases about Lane Restrictions and other Notifications
 - Monthly Progress Meetings (not open to the public)
 - On-Site Project Resident Engineer

➤ **Continued Coordination**

- **Working Group Meetings**
 - Meetings will shift from Quarterly to Monthly or at Project Milestones during Construction
 - Next Meeting – Spring 2013
- **Timely Updates on the Project Blog and Website**
 - www.SR26.deldot.gov

SR26, ATLANTIC AVE. FROM CLARKSVILLE TO ASSAWOMAN CANAL
DELDOT CONTRACT NO. T200411210
SR26 WORKING GROUP

THANK YOU

