

# SR26 WORKING GROUP

## Meeting No. 3

*May 20, 2013*

# *Opening Remarks*

PREPARED BY:  
**M CENTURY ENGINEERING**  
CONSULTING ENGINEERS, SURVEYORS  
454 N. DUPONT HWY.  
DURHAM, NC 27603  
(919) 286-9188

**DeDOT**


### SR 26, AREA IMPROVEMENTS PROJECT LIMITS AND CONSTRUCTION PHASING

500 SCALE  
(60" X 40")



JANUARY 2013

- LEGEND**
- DETOUR ROUTES
  - SR 26 MAINLINE
  - PARCELS
  - MILLVILLE
  - OCEAN VIEW
  - BETHANY BEACH
  - EARLY ACTION
  - CONSTRUCTION
  - BRIDGE
  - SECTION 1
  - SECTION 2
  - SECTION 3
  - SECTION 4

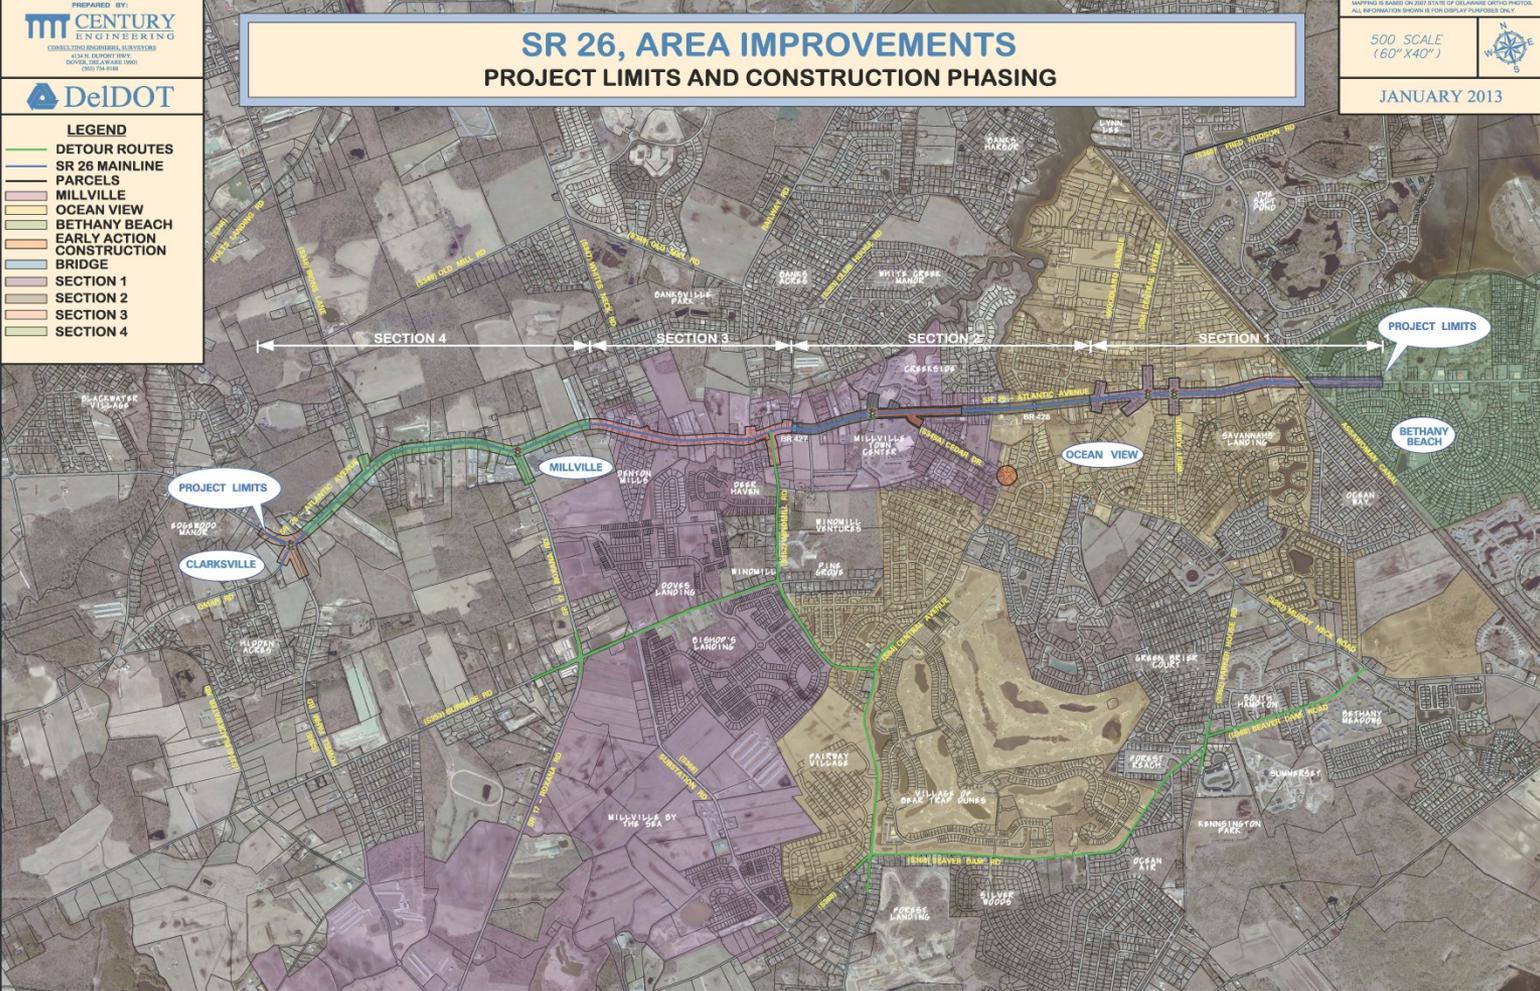

## ➤ **Agenda**

- **Introduction**
- **Project Status Update (SR 26 Detour Routes)**
  - Construction Update
- **Project Status Update (SR 26 Mainline)**
  - Utility Relocations
  - Advanced Clearing
  - Real Estate Acquisitions

## ➤ **Agenda**

- **Next Steps**
  - From now until Construction Begins
  - After Construction Begins

## ➤ **Agenda**

- **Project Public Outreach**
  - Before Construction
  - During Construction
- **SR 26 Project Website**
  - [www.SR26.deldot.gov](http://www.SR26.deldot.gov)
- **Continued Working Group Coordination**
  - Monthly to Quarterly Meetings

## ➤ Project Status

- **SR 26 Detour Routes**




- Project Accelerated
- FDR Started 5/13 on Windmill Road
- Work will continue on Beaver Dam Road and Central Avenue
- Paving will begin seven (7) days after FDR is complete

## ➤ Project Status

- SR26 Detour Routes




- Anticipate final paving to be completed by end of June 2013
- Entrance to Silverwoods subdivision to be completed after paving is completed
- Re-grade ditches and berms
- Topsoil and seed disturbed areas

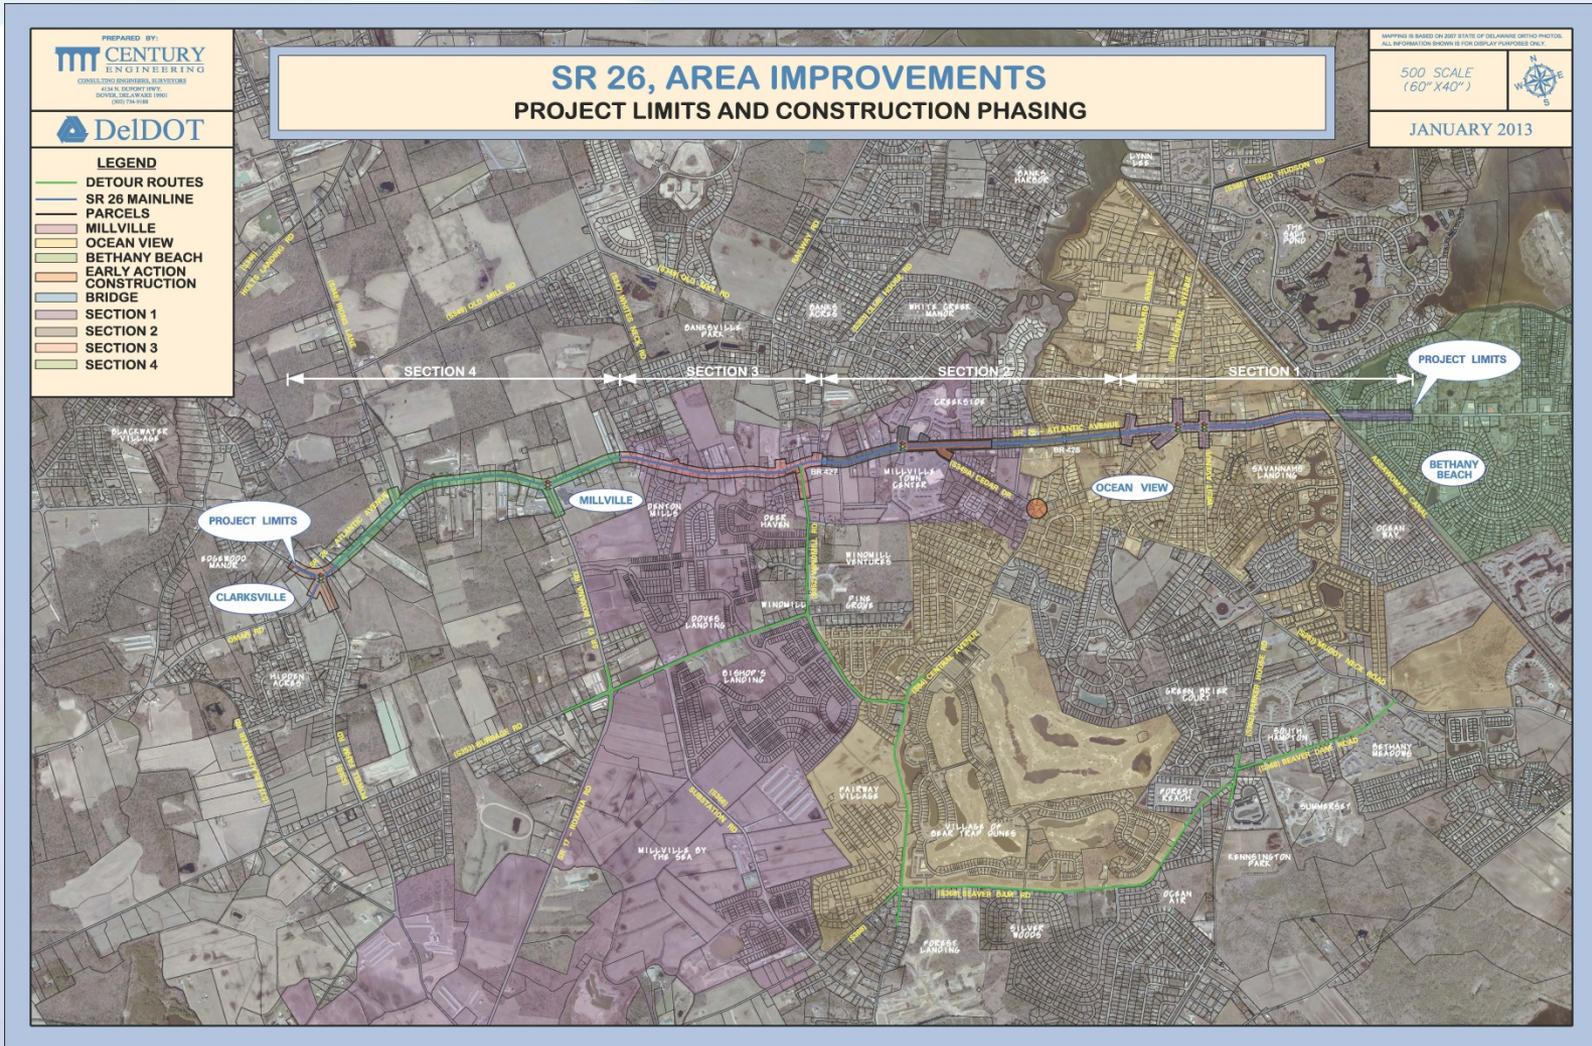

## ➤ Project Status

- Utility Relocations

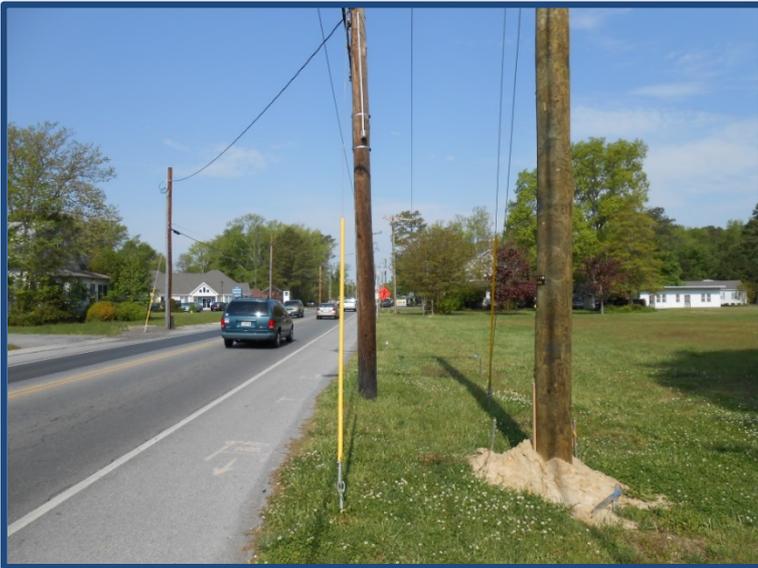

- 110 out of 250 utility poles have been replaced or relocated
- Work is completed in the Early Action Areas
- Clearing is completed in Sections 1 and 2
- Lane closures will continue until June 30

## ➤ Project Status

- **Real Estate Acquisitions**
  - One owner (3 parcels) outstanding
- **Advertisement**
  - Anticipate Advertisement in Summer 2013
- **Construction**
  - Anticipate Begin Construction in Fall 2013

## ➤ **Next Steps – Pre Award**

- **Final Plans**
  - Incorporating Sewer and Water Relocations
  - Incorporating Relocated Utility Poles
  - Coordinating with Entrance Improvements
  - Finalizing Alternative Routes and Detour Plans

## ➤ **Next Steps – Pre Award**

- **Award Inspection Contract**
  - Consultant Inspection Team
    - General and Specialty Inspection
    - Project Quantity Management
    - Community Support and Outreach
- **Project Advertisement**
  - Pre-Bid Meeting

## ➤ **Next Steps – Post Award**

- **Project Pre-Construction Meeting**
  - Review the Project Schedule
  - Review Phasing and Timing
- **Public Information Meeting**
  - Review Schedule
  - Review Alternative Routes
  - Coordination with Businesses
  - Design, Inspection, and Contractor Staff Available
  - Informational Brochure

## ➤ **Next Steps – Construction**

- Finish Clearing – Sections 3 and 4
- Remainder of Utility Relocations – Sections 3 and 4
- Construct Early Action Area – Clarksville and Cedar
- Construct Sewer FM Relocations in Ocean View

## ➤ **Project Public Outreach**

- **Before Construction**
  - Public Information Meeting
  - Continue Coordination with Chamber of Commerce
  - Continue Coordination with Emergency Services
- **On-Going Coordination**
  - Existing features within Right of Way
  - Property owner questions
  - Requests for Information

## ➤ **Project Public Outreach**

- **During Construction**
  - Press Releases about Lane Restrictions and other Notifications
  - SR 26 Project Information E-Mails
  - Monthly Progress Meetings with Contractor (not open to the public)
  - On-Site Project Resident Engineer

## ➤ **Continued Coordination**

- **Working Group Meetings**
  - Meetings will shift from Quarterly to Monthly or at Project Milestones during Construction
  - Next Meeting – Fall 2013
- **Timely Updates on the Project Blog and Website**
  - [www.SR26.deldot.gov](http://www.SR26.deldot.gov)

**THANK YOU**
